




| #  | Info | Title                            | Given Planned Duration | Given Planned Work | # Predecessors | Expected Start | Assigned Resources  | % Complete | Q3 / 2013 |    | Q4 / 2013                       |    |    |    |                                              |
|----|------|----------------------------------|------------------------|--------------------|----------------|----------------|---------------------|------------|-----------|----|---------------------------------|----|----|----|----------------------------------------------|
|    |      |                                  |                        |                    |                |                |                     |            | 08        | 09 | 10                              | 11 | 12 | 01 |                                              |
| 0  |      | Level-1-Trigger-Project-...      |                        |                    |                | 01/01/2014     | A Rose; M Gui...    | 0%         |           |    | Level-1-Trigger-Project-Plan-V8 |    |    |    |                                              |
| 1  |      | Preliminary Patch Panel Insta... | 1 week                 | 40 hours           |                | 17/03/2014     | T. Durkin           | 0%         |           |    |                                 |    |    |    | Preliminary Patch Panel                      |
| 3  |      | Preliminary System tests Lay...  | 2 weeks                | 440 hours          | 1              | 24/03/2014     | Tapper; Iles; T...  | 0%         |           |    |                                 |    |    |    | Preliminary System tests Layer-1/Layer-      |
| 10 |      | MP7 Production + 2 MP7s          | 1 month                | 24 hours           |                | 01/04/2014     | Iles                | 0%         |           |    |                                 |    |    |    | MI                                           |
| 12 |      | MP7 Testing firmware (MP7-...    | 1 month                | 160 hours          |                | 01/04/2014     | A Bundock           | 0%         |           |    |                                 |    |    |    | MP7 Testi                                    |
| 14 |      | MP7 Production + 4 MP7s an...    | 5 weeks                | 70 hours           | 10; 12         | 29/04/2014     | Iles; T. Durkin     | 0%         |           |    |                                 |    |    |    |                                              |
| 17 |      | MP7 Production + 10 MP7s a...    | 6 weeks                | 84 hours           | 14             | 03/06/2014     | Iles; A Bundock     | 0%         |           |    |                                 |    |    |    |                                              |
| 20 |      | Second MP7 production line...    | 13 weeks               | 182 hours          |                | 01/05/2014     | Iles; A Bundock     | 0%         |           |    |                                 |    |    |    | Second MI                                    |
| 23 |      | MP7 Production complete -...     |                        |                    | 17; 20         | 30/07/2014     |                     | 0%         |           |    |                                 |    |    |    |                                              |
| 24 |      | P5 DAQ DAQ1--> DAQ2 --...        | 31 days ?              |                    |                | 14/04/2014     |                     | 0%         |           |    |                                 |    |    |    | P5 DAQ DAC                                   |
| 25 |      | P5 DAQ2 Commissioning --...      | 26 days ?              |                    | 24             | 27/05/2014     |                     | 0%         |           |    |                                 |    |    |    |                                              |
| 26 |      | MP7 DAQ Interface Firmware       | 2 months               | 240 hours          |                | 01/04/2014     | Newbold; Das...     | 0%         |           |    |                                 |    |    |    | MP7                                          |
| 29 |      | Assembling DAQ testsetup,...     | 12 weeks               | 480 hours          |                | 01/04/2014     | K. Harder           | 0%         |           |    |                                 |    |    |    | Assembling DAQ testsetup                     |
| 31 |      | Final Version AMC13 Arrives...   |                        |                    |                | 02/06/2014     |                     | 0%         |           |    |                                 |    |    |    |                                              |
| 32 |      | Integration MP7-DAQ interfa...   | 4 weeks                | 320 hours          | 26; 31         | 02/06/2014     | Dasgupta; BU        | 0%         |           |    |                                 |    |    |    |                                              |
| 35 |      | Integration with DAQ2/XDA...     | 4 weeks                | 320 hours          | 25; 2...       | 02/07/2014     | Thea; K. Harder     | 0%         |           |    |                                 |    |    |    |                                              |
| 38 |      | MP7 Data unpacker                | 1 month                | 320 hours          |                | 01/04/2014     | Tapper; Brooke      | 0%         |           |    |                                 |    |    |    |                                              |
| 41 |      | MP7 - DAQ Interface and Da...    |                        |                    | 35; 38         | 29/07/2014     |                     | 0%         |           |    |                                 |    |    |    |                                              |
| 42 |      | Firmware for MP7->Legacy...      | 6 weeks                | 240 hours          | 3              | 07/04/2014     | Iles                | 0%         |           |    |                                 |    |    |    | Firmware for MP7->Legacy GT-oGT1 3 G         |
| 44 |      | DEMUX Firmware                   | 1 month                | 80 hours           | 42             | 19/05/2014     | Iles                | 0%         |           |    |                                 |    |    |    |                                              |
| 46 |      | Installation and PC connectio... | 2 weeks                | 80 hours           | 31             | 16/06/2014     | Iles; Thea          | 0%         |           |    |                                 |    |    |    | Inst                                         |
| 49 |      | Integration with Legacy GT       | 1 week                 | 80 hours           | 44; 46         | 30/06/2014     | Iles; Jeitler       | 0%         |           |    |                                 |    |    |    |                                              |
| 52 |      | Interface of 2016 Trigger La...  |                        |                    | 49             | 04/07/2014     |                     | 0%         |           |    |                                 |    |    |    |                                              |
| 53 |      | Installation of the 12 Layer-... | 1 week                 | 40 hours           | 17             | 15/07/2014     | T. Durkin           | 0%         |           |    |                                 |    |    |    |                                              |
| 55 |      | 2016 Trigger Layer-2 12 MP...    |                        |                    | 53             | 21/07/2014     |                     | 0%         |           |    |                                 |    |    |    |                                              |
| 56 |      | First Version of the CMSSW E...  | 1 month                | 352 hours          |                | 17/03/2014     | J Baptist; S Har... | 0%         |           |    |                                 |    |    |    | First Version of the CMS                     |
| 60 |      | First Version of the CMSSW...    | 8 weeks                | 640 hours          |                | 17/03/2014     | Luca Mastrolor...   | 0%         |           |    |                                 |    |    |    | First Version of the CMS                     |
| 63 |      | First version of the CMSSW J...  | 2 months               | 480 hours          |                | 17/03/2014     | J Marrouche; B...   | 0%         |           |    |                                 |    |    |    | First version of the CMSSW Jet/MET/MHT/Ht/Et |
| 66 |      | First Version Firmware of 20...  | 7 weeks                | 420 hours          |                | 17/03/2014     | A Rose; Thierry     | 0%         |           |    |                                 |    |    |    | First Version Firmware of 2016 Trigg         |
| 69 |      | First Version Firmware of the... | 1 month                | 240 hours          | 66             | 05/05/2014     | A Rose; Thierry     | 0%         |           |    |                                 |    |    |    | First Version                                |
| 72 |      | First Version of Jet/MET/MH...   | 4 weeks                | 80 hours           |                | 17/03/2014     | A Rose              | 0%         |           |    |                                 |    |    |    | First Version of Jet/MET/MHT/Et/Ht Tr        |
| 74 |      | Pattern Testing of Jet/MET/...   | 6 weeks                | 120 hours          | 56; 72         | 14/04/2014     | A Rose              | 0%         |           |    |                                 |    |    |    | Pattern Testing of Jet/MET/A                 |

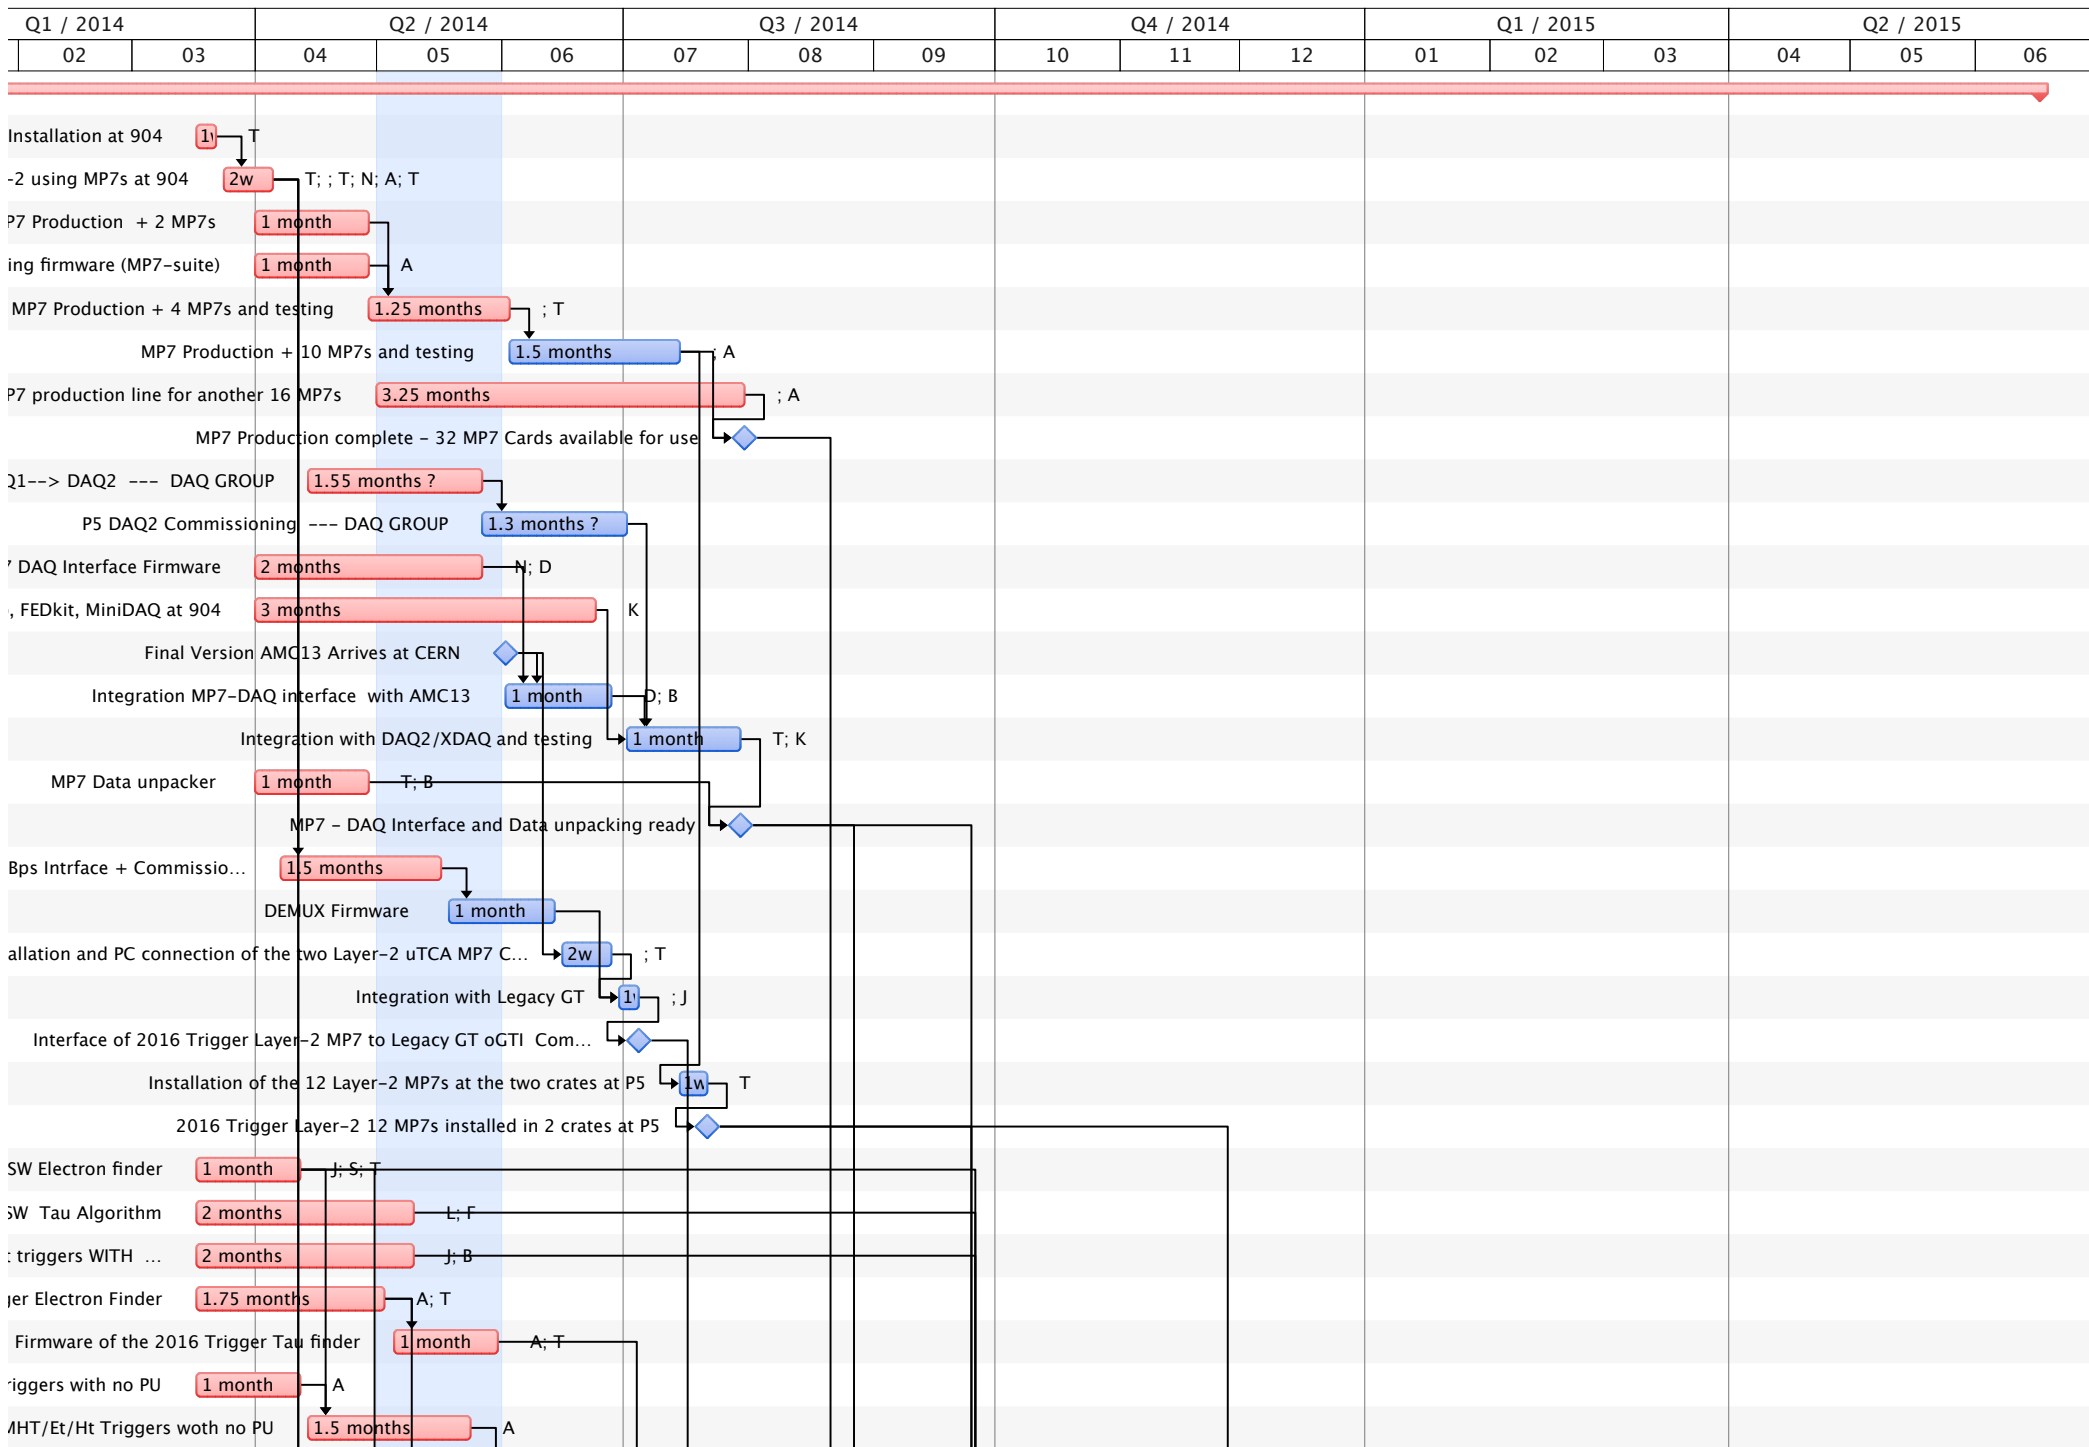

|     |                                   |          |           |          |            |                    |    |   |  |                                         |
|-----|-----------------------------------|----------|-----------|----------|------------|--------------------|----|---|--|-----------------------------------------|
| 76  | First Version Firmware for th...  | 6 weeks  | 240 hours | 74       | 26/05/2014 | A Rose             | 0% | ⌵ |  | First Version F                         |
| 78  | Pattern Tests for Commissio...    | 1 month  | 360 hours | 56; 66   | 05/05/2014 | Thierry; Zabi;...  | 0% | ⌵ |  | Pattern Tests for Comr                  |
| 82  | Pattern Tests for Commissio...    | 6 weeks  | 360 hours | 78       | 02/06/2014 | A Bundock; J...    | 0% | ⌵ |  | Pattern Tests                           |
| 85  | Development of Version 1 of...    |          |           | 69; 7... | 11/07/2014 |                    | 0% | ⌵ |  |                                         |
| 86  | ⌵ CTP7 Prototype testing          | 12 weeks | 480 hours |          | 01/04/2014 | Gorski             | 0% | ⌵ |  |                                         |
| 88  | CTP7 Pre-Production of 3-4...     | 1 month  | 24 hours  | 86       | 24/06/2014 | Gorski             | 0% | ⌵ |  |                                         |
| 90  | CTP7 Pre-Production testing       | 1 month  | 160 hours | 88       | 22/07/2014 | Gorski             | 0% | ⌵ |  |                                         |
| 92  | ⌵ Final CTP7 production           | 4 weeks  |           | 90       | 01/10/2014 |                    | 0% | ⌵ |  |                                         |
| 93  | Final CTP7 Production testing     | 4 weeks  |           | 92       | 29/10/2014 |                    | 0% | ⌵ |  |                                         |
| 94  | ⌵ Shipping 3-4 Pre-productio...   | 1 week   |           | 90       | 19/08/2014 |                    | 0% | ⌵ |  |                                         |
| 95  | 3-4 Pre-Production CTP7s at...    |          |           | 94       | 25/08/2014 |                    | 0% | ⌵ |  |                                         |
| 96  | Shipping production CTP7s t...    | 1 week   |           | 93       | 26/11/2014 |                    | 0% | ⌵ |  |                                         |
| 97  | ⌵ CTP7 Production complete -...   |          |           | 96       | 02/12/2014 |                    | 0% | ⌵ |  |                                         |
| 98  | ⌵ CTP7 Service firmware+ Dat...   | 4 months | 640 hours |          | 01/04/2014 | Marcelo            | 0% | ⌵ |  | CTP7 Service firmware+ Data pass-throug |
| 100 | ⌵ oSLB/uHTR-->CTP7-->MP7...       | 2 weeks  | 640 hours | 52; 98   | 22/07/2014 | Iles; Da Silva;... | 0% | ⌵ |  |                                         |
| 109 | Slice Test oSLB/oRM--CTP7-...     |          |           | 100      | 04/08/2014 |                    | 0% | ⌵ |  |                                         |
| 110 | Firmware CTP7 Layer-1 TMT...      | 2 months | 320 hours | 109      | 05/08/2014 | Svetek             | 0% | ⌵ |  |                                         |
| 112 | Firmware CTP7 Layer-1 TMT...      | 2 months | 160 hours | 110      | 30/09/2014 | Svetek             | 0% | ⌵ |  |                                         |
| 114 | Layer-1 Firmware Developm...      |          |           | 112      | 24/11/2014 |                    | 0% | ⌵ |  |                                         |
| 115 | Firmware for testing the Patc...  | 2 months | 320 hours | 3        | 07/04/2014 | A Bundock          | 0% | ⌵ |  | Firmware for testing the Patch P        |
| 117 | ⌵ Layer-1 - Layer -2 Patch Pan... | 12 weeks | 72 hours  | 3        | 07/04/2014 | T. Durkin          | 0% | ⌵ |  | Layer-1 - Layer                         |
| 119 | ⌵ Layer-1 - Layer -2 Patch-Pa...  | 4 weeks  | 160 hours | 117      | 30/06/2014 | T. Durkin          | 0% | ⌵ |  |                                         |
| 121 | Layer-1 - Layer-2 Patch Pan...    | 1 week   |           | 119      | 28/07/2014 |                    | 0% | ⌵ |  |                                         |
| 122 | Layer-1 - Layer-2 Patch Pan...    | 1 week   | 40 hours  | 121      | 04/08/2014 | T. Durkin          | 0% | ⌵ |  |                                         |
| 124 | ⌵ oSLB/uHTR Patch Panel Design    | 1 month  |           |          | 01/04/2014 |                    | 0% | ⌵ |  | oSLB/                                   |
| 125 | oSLB/uHTR Patch Panel man...      | 12 weeks |           | 124      | 29/04/2014 |                    | 0% | ⌵ |  | oSLB/uHTR Patcl                         |
| 126 | oSLB/oRM Patch Panel Trans...     | 1 week   |           | 125      | 22/07/2014 |                    | 0% | ⌵ |  |                                         |
| 127 | oSLB/uHTR to Layer -1 Patch...    | 2 weeks  |           | 109;...  | 05/08/2014 |                    | 0% | ⌵ |  |                                         |
| 128 | Layer-1 Crate Installation (6...  | 2 weeks  |           | 109;...  | 11/08/2014 |                    | 0% | ⌵ |  |                                         |
| 129 | ⌵ Commissioning of Layer-2 a...   | 2 weeks  | 160 hours | 23; 9... | 26/08/2014 | A Bundock; T....   | 0% | ⌵ |  |                                         |
| 132 | Layer-2 + Patch Panel + 1/9...    |          |           | 129      | 08/09/2014 |                    | 0% | ⌵ |  |                                         |
| 133 | ⌵ Integration of the 2016 Trig... | 2 weeks  | 400 hours | 41; 100  | 01/09/2014 | Dasgupta; Tap...   | 0% | ⌵ |  |                                         |
| 139 | Layer-2 + Patch Panel + 1/9...    |          |           | 133      | 12/09/2014 |                    | 0% | ⌵ |  |                                         |
| 140 | Commissioning of 2016 Trig...     | 9 weeks  | 900 hours | 41; 5... | 30/09/2014 | A Rose; A Bun...   | 0% | ⌵ |  |                                         |

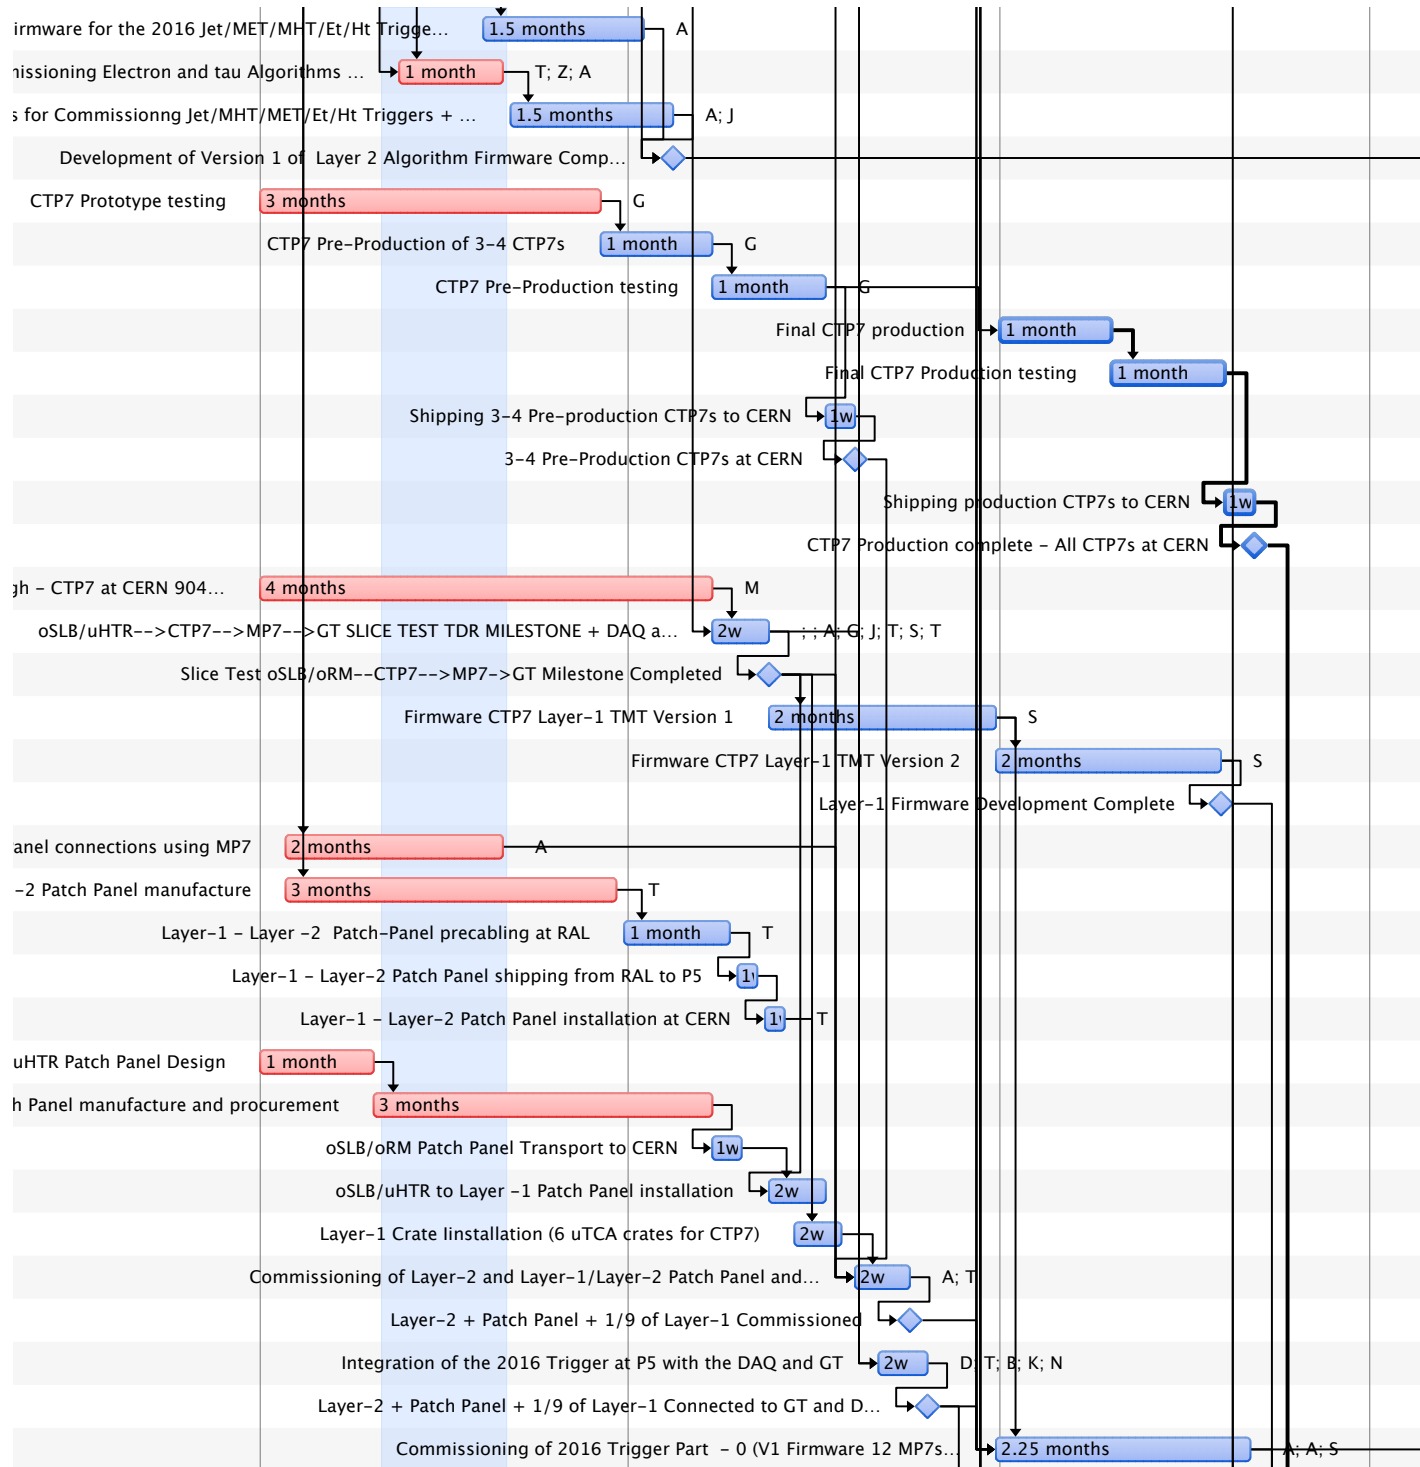

|     |                                  |           |             |          |            |                     |    |   |                                                              |                     |
|-----|----------------------------------|-----------|-------------|----------|------------|---------------------|----|---|--------------------------------------------------------------|---------------------|
| 144 | Commissioning – 12 MP7+ 3...     | 2 months  | 960 hours   | 55; 9... | 03/12/2014 | A Rose; A Bun...    | 0% | ⌵ |                                                              |                     |
| 148 | 2016 Trigger Ready for recei...  |           |             | 144      | 27/01/2015 |                     | 0% | ⌵ |                                                              |                     |
| 149 | Commissioning HCAL B/E u...      | 5 months  |             | 148      | 28/01/2015 |                     | 0% | ⌵ |                                                              |                     |
| 150 | Online Monitoring Software f...  | 6 months  |             | 139      | 15/09/2014 |                     | 0% | ⌵ |                                                              |                     |
| 151 | 2016 Trigger final Emulators     | 4 months  |             | 56; 6... | 01/10/2014 |                     | 0% | ⌵ |                                                              |                     |
| 152 | Final Firmware for the 2016...   | 4 months  |             | 85; 1... | 21/01/2015 |                     | 0% | ⌵ |                                                              |                     |
| 153 | 2016 Trigger Ready for Data...   |           |             | 149;...  | 16/06/2015 |                     | 0% | ⌵ |                                                              |                     |
| 154 | ORSc Firmware – V1 for the...    | 83 days   | 597.6 ho... |          | 01/01/2014 | Svetek; Matias      | 0% | ⌵ | ORSc Firmware – V1 for the APRIL2014 RCT->ORSc->MP7 test     | 4.15 months         |
| 157 | ORSc Testing software for th...  | 83 days   | 1,328 ho... |          | 01/01/2014 | Klabbers; Cali      | 0% | ⌵ | ORSc Testing software for the April-2014 RCT->ORSc->MP7 test | 4.15 months         |
| 160 | RCT-ORSc-MP7 -- Integrat...      | 3 weeks   | 240 hours   | 154;...  | 28/04/2014 | Svetek; Cali; Kl... | 0% | ⌵ |                                                              | RCT-ORSc-MP7 -- Int |
| 165 | ORSCs Integrated with RCT a...   |           |             | 160      | 16/05/2014 |                     | 0% | ⌵ |                                                              | ORSCs Integratec    |
| 166 | ORSc Firmware for Integratio...  | 1 month   | 192 hours   | 165      | 19/05/2014 | Iles; Marcelo       | 0% | ⌵ |                                                              |                     |
| 169 | OSCs integration tests with L... | 1 month   | 192 hours   | 166      | 16/06/2014 | Iles; Marcelo       | 0% | ⌵ |                                                              |                     |
| 172 | ORSCs Integrated with Legac...   |           |             | 169      | 11/07/2014 |                     | 0% | ⌵ |                                                              |                     |
| 173 | 1st Global Run April 7.4 – 11.4  | 5 days ?  |             |          | 07/04/2014 |                     | 0% | ⌵ |                                                              | 1st C               |
| 174 | ORSc Production                  | 1 month   | 80 hours    | 165      | 19/05/2014 | Gorski              | 0% | ⌵ |                                                              |                     |
| 176 | ORSc Testing at Madison          | 1 month   | 160 hours   | 174      | 16/06/2014 | Gorski              | 0% | ⌵ |                                                              |                     |
| 178 | Easter Week 18.4 – 21.4          | 2 days ?  |             |          | 18/04/2014 |                     | 0% | ⌵ |                                                              |                     |
| 179 | Power off at P5                  | 16 days ? |             |          | 29/04/2014 |                     | 0% | ⌵ |                                                              |                     |
| 180 | Commissioning Software tes...    | 1 month   | 160 hours   | 157      | 28/04/2014 | GM Innocenti        | 0% | ⌵ |                                                              | Commissioning S     |
| 182 | Installation of uTCA Crate at... | 2 weeks   | 80 hours    | 165      | 19/05/2014 | Iles                | 0% | ⌵ |                                                              |                     |
| 184 | ORSCs Testing complete           |           |             | 176      | 11/07/2014 |                     | 0% | ⌵ |                                                              |                     |
| 185 | ORSc transport US-->CERN         | 1 week    |             | 184      | 14/07/2014 |                     | 0% | ⌵ |                                                              |                     |
| 186 | ORSc Installation at P5 inclu... | 1 month   | 320 hours   | 182;...  | 21/07/2014 | Cali; Klabbers      | 0% | ⌵ |                                                              |                     |
| 189 | Comissioning ECAL/HCAL/O...      | 20 days   | 160 hours   | 172;...  | 18/08/2014 | Cali                | 0% | ⌵ |                                                              |                     |
| 191 | ORSCs Installation and testin... |           |             | 189      | 12/09/2014 |                     | 0% | ⌵ |                                                              |                     |
| 192 | ORSc firmware for running S...   | 2 months  | 320 hours   | 165      | 19/05/2014 | Guo                 | 0% | ⌵ |                                                              |                     |
| 194 | ORSc Firmware for running t...   | 2 months  | 320 hours   | 172;...  | 14/07/2014 | Marcelo             | 0% | ⌵ |                                                              |                     |
| 196 | 2nd Global Run 3.7 – 10.7.2014   | 6 days ?  |             |          | 03/07/2014 |                     | 0% | ⌵ |                                                              |                     |
| 197 | Comm the Legacy Running v...     | 1 month   | 360 hours   | 191;...  | 15/09/2014 | Iles; Thea; Ma...   | 0% | ⌵ |                                                              |                     |
| 201 | Legacy System Can Trigger...     |           |             | 197      | 10/10/2014 |                     | 0% | ⌵ |                                                              |                     |
| 202 | Comissioning of the Stage-1...   | 1 month   | 400 hours   | 191;...  | 13/10/2014 | Guo; Cali; Klab...  | 0% | ⌵ |                                                              |                     |
| 206 | Stage-1 Comm. In Parallel...     |           |             | 202      | 07/11/2014 |                     | 0% | ⌵ |                                                              |                     |
| 207 | ORSc firmware for testing+V...   | 2 months  | 320 hours   | 206      | 10/11/2014 | Marcelo             | 0% | ⌵ |                                                              |                     |

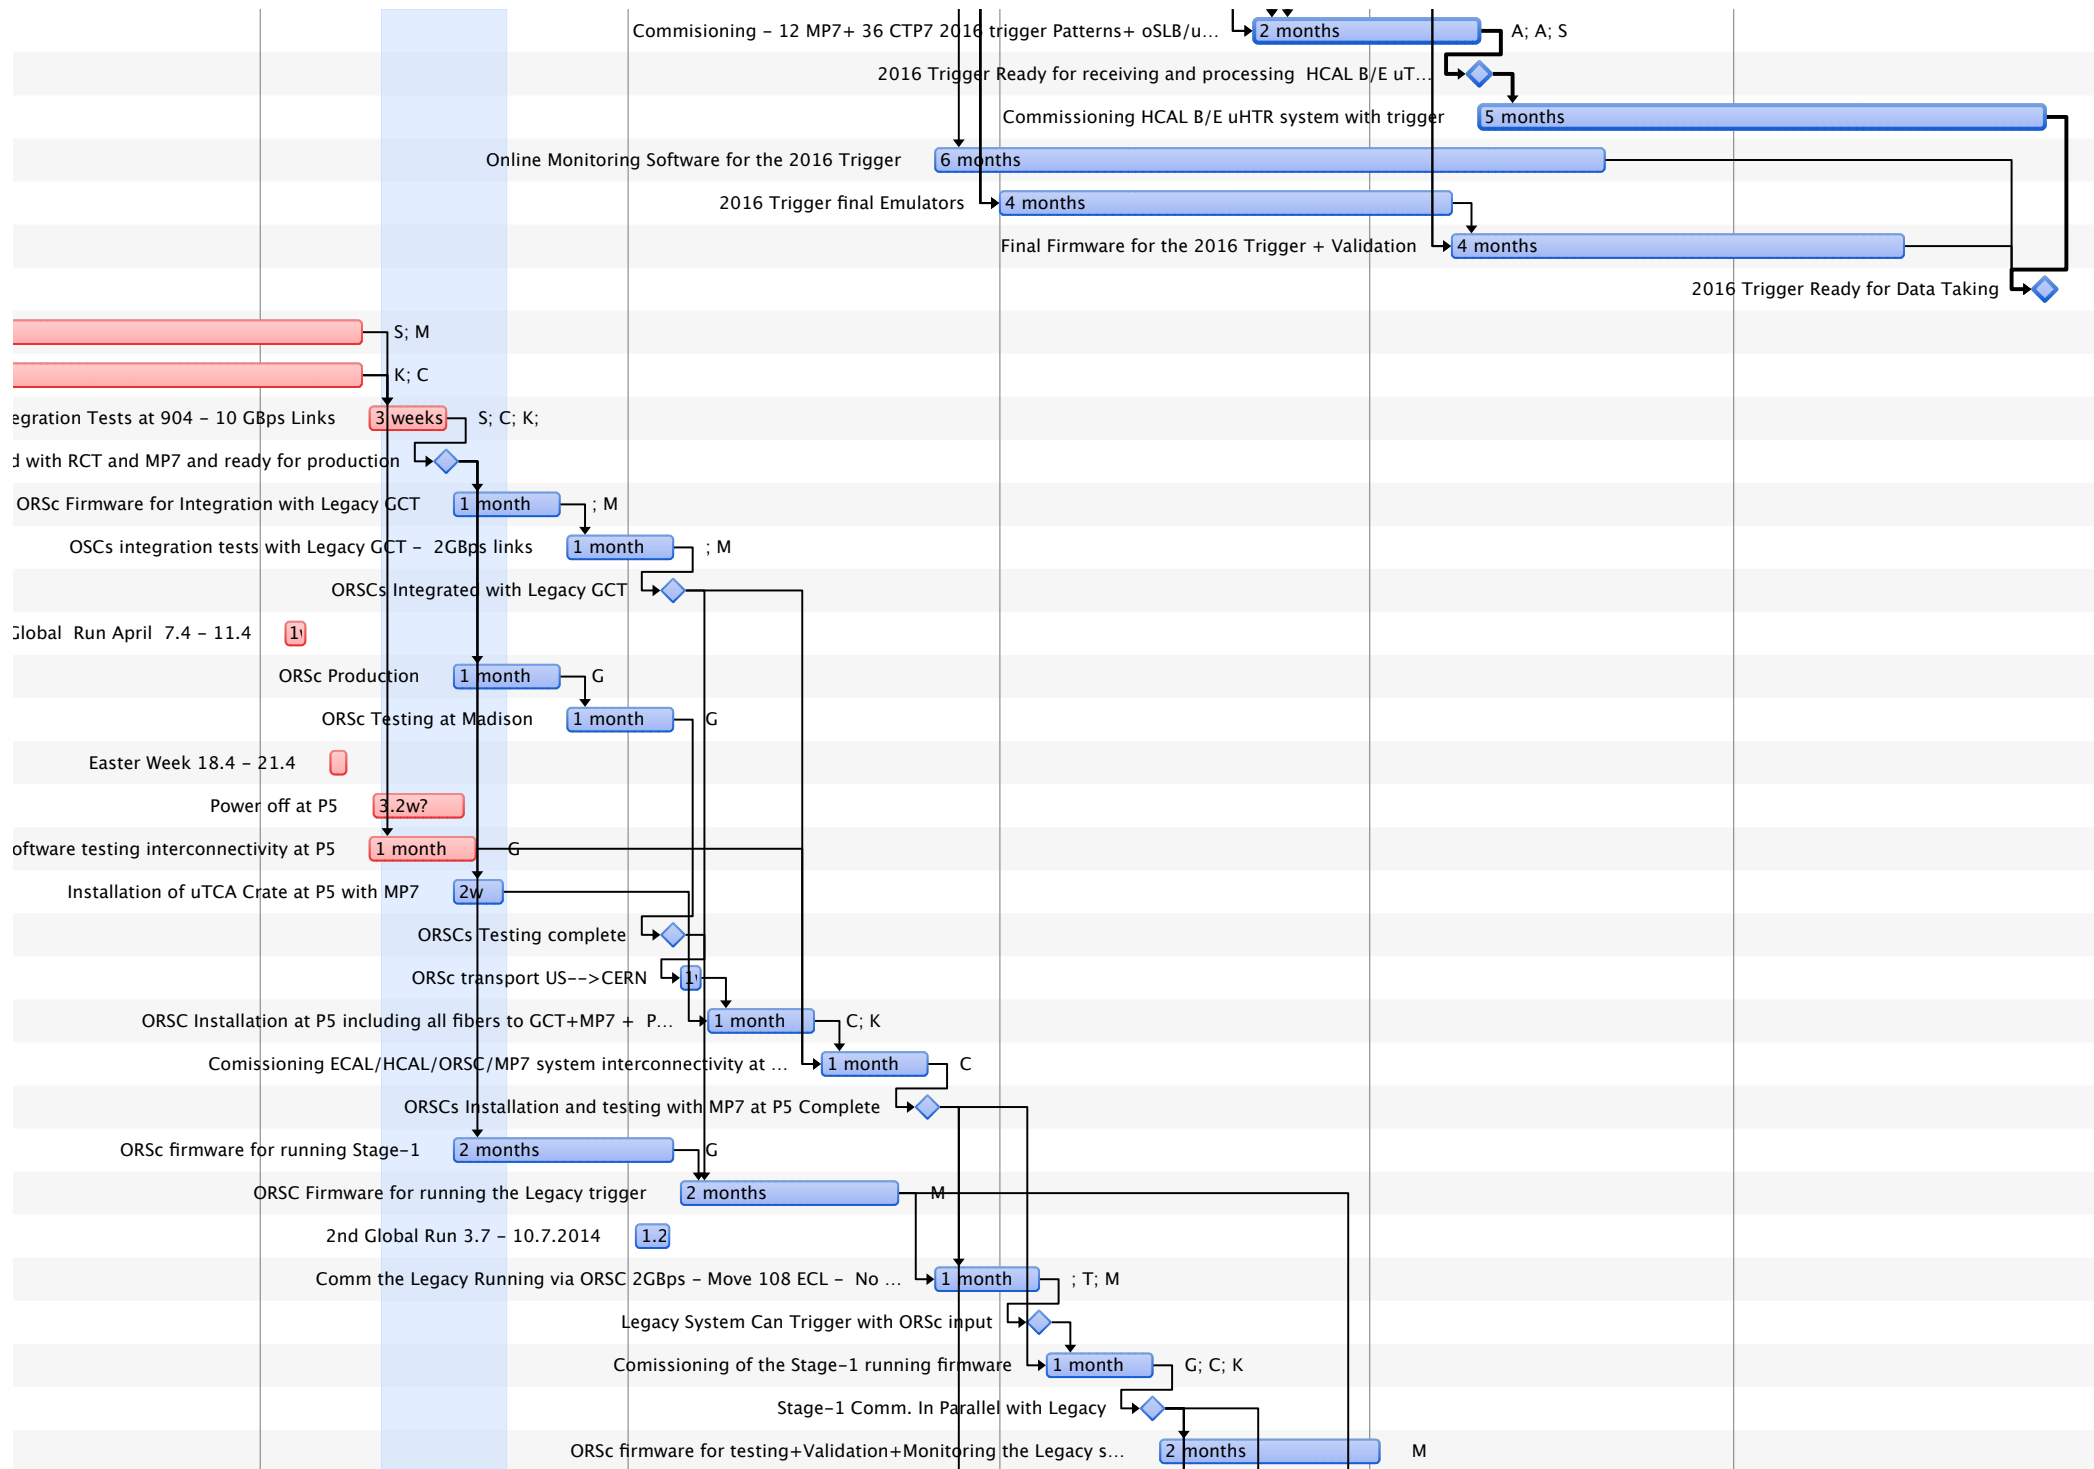

|     |                                   |           |             |         |            |                   |    |   |                                                          |              |
|-----|-----------------------------------|-----------|-------------|---------|------------|-------------------|----|---|----------------------------------------------------------|--------------|
| 209 | ORSc Software for testing+V...    | 2 months  | 480 hours   | 206     | 10/11/2014 | Thea; M Guilbaud  | 0% | ⌵ |                                                          |              |
| 212 | Legacy System Fully Integrat...   |           |             | 194;... | 02/01/2015 |                   | 0% | ⌵ |                                                          |              |
| 213 | Electron and Tau Algorithm...     | 6 months  | 960 hours   |         | 01/04/2014 | Firmware Engi...  | 0% | ⌵ | Electron and Tau Algorithm Firmw                         |              |
| 215 | Electron and Tau Algorithm...     | 2 months  | 320 hours   | 191;... | 16/09/2014 | Firmware Engi...  | 0% | ⌵ |                                                          |              |
| 217 | Electron and Tau Algorithm...     | 1 month   |             | 215     | 11/11/2014 |                   | 0% | ⌵ |                                                          |              |
| 218 | Electron and Tau Trigger Val...   | 3 months  | 960 hours   | 217     | 09/12/2014 | Firmware Engi...  | 0% | ⌵ |                                                          |              |
| 221 | Monitoring Software for Stag...   | 4 months  | 640 hours   | 206     | 10/11/2014 | GM Innocenti      | 0% | ⌵ |                                                          |              |
| 223 | Electron/Tau Triggers Ready...    |           |             | 218;... | 02/03/2015 |                   | 0% | ⌵ |                                                          |              |
| 224 | Jet+MET+MHT Algorithm Fir...      | 6 months  | 960 hours   |         | 01/04/2014 | Firmware Engi...  | 0% | ⌵ | Jet+MET+MHT Algorithr                                    |              |
| 226 | JET+MET+MHT Algorithm pr...       | 3 months  | 480 hours   | 224     | 16/09/2014 | Firmware Engi...  | 0% | ⌵ |                                                          |              |
| 228 | JET+MET+MHT Firmware Co...        | 1 month   | 160 hours   | 206;... | 09/12/2014 | Firmware Engi...  | 0% | ⌵ |                                                          |              |
| 230 | JET+MET+MHT Trigger Valid...      | 3 months  | 960 hours   | 228     | 06/01/2015 | Firmware Engi...  | 0% | ⌵ |                                                          |              |
| 233 | Monitoring Software for Stag...   | 4 months  |             | 206     | 10/11/2014 |                   | 0% | ⌵ |                                                          |              |
| 234 | STAGE-1 MET/MHT/JETS AN...        |           |             | 230;... | 30/03/2015 |                   | 0% | ⌵ |                                                          |              |
| 235 | oSLB - 650 - JTAG testing         | 1 month   | 160 hours   |         | 06/01/2014 | Anatoli           | 0% | ⌵ | oSLB - 650 - JTAG testing                                | 1 month      |
| 237 | oSLB - 650 - Programming -...     | 1 month   | 200 hours   | 235     | 03/02/2014 | Marcelo; Da Silva | 0% | ⌵ | oSLB - 650 - Programming - functionality testing - Links |              |
| 240 | oSLB testing finished             |           |             | 237     | 28/02/2014 |                   | 0% | ⌵ |                                                          | oSLB testing |
| 241 | oRM - 650 - JTAG testing an...    | 1 month   | 160 hours   |         | 12/02/2014 | Anatoli           | 0% | ⌵ | oRM - 650 - JTAG testing and Link testi                  |              |
| 243 | oRM - 650 - functionality te...   | 1 month   | 320 hours   | 241     | 12/03/2014 | Marcelo; Klabb... | 0% | ⌵ | oRM - 650 - functionality                                |              |
| 247 | oRM Testing Finished              |           |             | 243     | 08/04/2014 |                   | 0% | ⌵ |                                                          |              |
| 248 | oSLB TCC oRM/CTP7 + uHT...        | 1 month   | 226.67 h... |         | 24/02/2014 | Yannick ; Da S... | 0% | ⌵ | oSLB TCC oRM/CTP7 + uHTR/CTP7 oRM Integration tests at   |              |
| 252 | Last TCC/oSLB/oRM/RC/HT...        | 2 weeks   | 280 hours   | 248     | 24/03/2014 | Klabbers; Da...   | 0% | ⌵ | Last TCC/oSLB/oRM/RC/HTR-HCAL integratio                 |              |
| 257 | oSLB/oRM system ready for I...    |           |             | 237;... | 08/04/2014 |                   | 0% | ⌵ | oSLB/oRM system ready for I                              |              |
| 258 | 1ST GLOBAL RUN 7.4 - 11.4...      | 1 week    |             |         | 07/04/2014 |                   | 0% | ⌵ | 1ST GLOBAL RUN 7.4 - 11.4 - Le                           |              |
| 259 | Removing ECAL Trigger Cabl...     | 1 week    | 120 hours   | 257;... | 14/04/2014 | Zabi; LLR-Tec...  | 0% | ⌵ | Removing ECAL Trigger Cabl                               |              |
| 263 | Easter Vacation Cern Closed...    | 2 days ?  |             |         | 18/04/2014 |                   | 0% | ⌵ |                                                          | Easter \     |
| 264 | Power off at P5 29.4 - 20.5       | 16 days ? |             |         | 29/04/2014 |                   | 0% | ⌵ |                                                          |              |
| 265 | Removing ECAL Trigger Cab...      | 1 week    | 120 hours   | 257;... | 22/04/2014 | Zabi; LLR-Tec...  | 0% | ⌵ | Removing ECAL Trigger C                                  |              |
| 269 | Fiber Installation etc that re... | 3 weeks   | 360 hours   | 265     | 29/04/2014 | LLR-Tech-1; Z...  | 0% | ⌵ |                                                          | Fiber Instal |
| 273 | oSLB - oRM installation and...    | 30 days   | 1,200 ho... | 269     | 20/05/2014 | Da Silva; Klab... | 0% | ⌵ |                                                          | oSLB - oRM i |
| 279 | oSLB-oRM Interface Ready fo...    |           |             | 273     | 30/06/2014 |                   | 0% | ⌵ |                                                          |              |
| 280 | 2ND GLOBAL RUN 3.7 - 10.7...      | 6 days ?  |             |         | 03/07/2014 |                   | 0% | ⌵ |                                                          | 2N           |

